



PFM Construction Inc.
23089 Muench Trail,
Langley, BC
V1M 4G6

Supervisor Daily Report

Information

 May 15 2026, Detention Tank Installations (revision)

 Chandos 1st & Clark

 Sunday, May 17th 2026, 3:43 PM (PDT -07:00)

General Information

Project Name:  East 1st & Clark



Date:  May 15, 2026

Supervisor:  Allen Goodman



Project Number:  25-C13

Location:  1st and Clark



Active work area
(outlined in green) is
located along the
southern boundary of
the site, running
parallel to East 1st
Avenue.

Weather:

 Raining

Labour

Name:  Allen Goodman

Position/Trade:

 Foreman

Start Time:  07:30 am

Finish Time:  03:00 pm

Scope Code:

 1st and Clark ► OFF-STM-DET-TANK

Comments:

 No Response

Labour

Name:  Kurt Sandergaard

Position/Trade:

 Operator

Start Time:  07:30 am

Finish Time:  03:00 pm

Scope Code:

 1st and Clark ► OFF-STM-DET-TANK

Comments:

 No Response

Labour

Name:  Robert Campeau

Position/Trade:

 Labourer

Start Time:  07:30 am

Finish Time:  03:00 pm

Scope Code:

 1st and Clark ► OFF-STM-DET-TANK

Comments:

 No Response

Labour	
Name:	 Karan Ghuman
Position/Trade: ☒ Labourer	
Start Time:	 07:30 am
Finish Time:	 03:00 pm
Scope Code: ☒ 1st and Clark ► OFF-STM-DET-TANK	
Comments:  No Response	
Labour	
Name:	 Jamal Elsaka
Position/Trade: ☒ Labourer	
Start Time:	 07:30 am
Finish Time:	 03:00 pm
Scope Code: ☒ 1st and Clark ► OFF-STM-DET-TANK	
Comments:  No Response	
Equipment	
Equipment Description:	 JD 60 excavator
Quantity:	 1
Hours Used:	 7.5
Scope Code: ☒ 1st and Clark ► OFF-STM-DET-TANK	
Condition/Comments:  No Response	



Equipment

Equipment Description: = JD 331 skid steer

Quantity: # 1


Hours Used: # 8

Scope Code:

✓ 1st and Clark ► OFF-STM-DET-TANK

Condition/Comments:

☰ No Response



Equipment

Equipment Description: = 1000lb packer

Quantity: # 1

Hours Used: # 8

Scope Code:

✓ 1st and Clark ► OFF-STM-DET-TANK

Condition/Comments:

☰ No Response



Materials

Material Description: = None

Quantity: # 0

Unit of Measure: = None

Comments:

≡ No Response

Subcontractors

Company Name: = None

Scope of Work: = None

Hours Worked: # 0

Comments:

≡ No Response

Work Performed

Jobsite Activities:

≡ FLHA

- Discussed tasks with crew members in the morning meeting so they were aware of the plan for our day
- Went over hazards we could encounter with our scope of work
- Site specific safety orientation

EXCAVATION

- Removed riser and base from hole to allow for base to be lowered so invert was on design
- Hand Shovel base gravel to right elevation
- Graded out slab for manhole prep

MISCELLANEOUS

- Tool set up and prep for the day
- Site clean up / house keeping
- Watering materials for dust control
- Hand Shovel manhole base
- Spotting equipment
- Unloaded equipment that was delivered
- Mobilized equipment to our work area
- Built pad by hand because machine could not fit in the work area

-Set up grades for manhole prep

IMPORT/EXPORT

None

DISCUSSION/NOTES

- Asked for crane to lift riser over
- Was informed by Rob that scaffold was to be taken down Tuesday

Progressed Quantities

Progress:

☒ 1st and Clark ► OFF-STM-DET-TANK

 Following a grade check of the storm detention tank manhole, the precast base section was removed and the subgrade lowered to ensure the installation aligns perfectly with the required design invert elevation.

Quantities Completed: # 1

Unit of Measure:

☒ each

Site Conditions/Issues/Delays

Comments:

 The only delay today was a temporary wait for the crane to become available to lift the manhole barrel riser from the laydown area.

Safety and Inspection

☒ Yes ☐ No ☐ NA Toolbox Talk Completed:

☐ Yes ☒ No ☐ NA Incidents/Accidents:

☒ Yes ☐ No ☐ NA Inspections Conducted:

Visitors

Name: = Marco

Company: = PFM Construction

Purpose of Visit:

 Site check up

Comments/Additional Notes

Additional Photos





The lane shown serves as the primary access route for both the main site and our specific work zone. Because the space accommodates one vehicle at a time, coordinating our activities around other scheduled project deliveries will be important to maintain a steady workflow and avoid potential timeline impacts.



Precast concrete structures have been delivered and staged on-site. Final installation into position will require a crane lift to ensure safe handling and precise placement within the active work area.



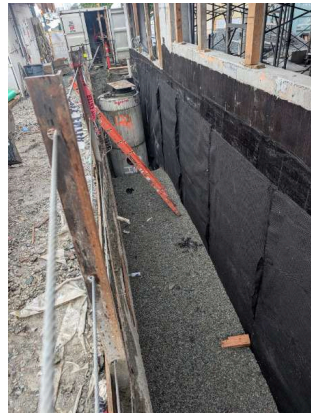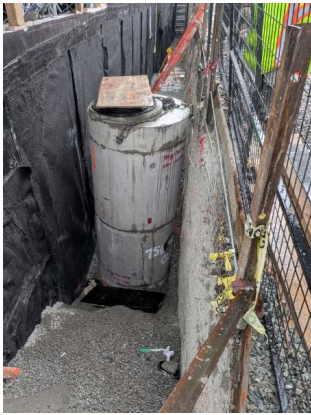


Active concrete pouring operations taking place on-site, requiring coordinated use of the corridor alongside structural shoring and crane work. The shoring is scheduled to be taken down on Tuesday following the long weekend.

Original

Allen Goodman, IC Operator

 May 17th 2026, 3:43 PM (PDT -07:00)



Revised on May 17th 2026, 3:44 PM (PDT -07:00)

Current View

Allen Goodman, IC Operator

 May 17th 2026, 3:44 PM (PDT -07:00)

